


PHASE 1:

- VACATE BUILDINGS 'A & B'
- SCHOOL OCCUPIES BUILDINGS 'C, D & E' (TOTAL AVAILABLE CLASSROOMS = 26-27)
- SEISMIC UPGRADES AND FUNCTIONAL ALTERATIONS TO BUILDINGS 'A & B'
- COMPLETE MAJOR BOILER, MECHANICAL & ELECTRICAL UPGRADES
- DEMOLISH 1 STOREY BLOCK AT SOUTH END OF BUILDING 'A'
- CONSTRUCT UPGRADED CONNECTION BETWEEN BUILDINGS 'A & B'

PHASE 2:

- RE-OCCUPY BUILDINGS 'A & B' FOR NEW SCHOOL USES
- VACATE BUILDING 'C'
- USE BUILDINGS 'D & E' FOR CLASSROOM SWING SPACE. (TOTAL AVAILABLE CLASSROOMS = 23-26)
- COMPLETE ALL UPGRADES TO BUILDING 'C'
- COMPLETE FINAL SITEWORKS/PLAY SPACE ALTERATIONS

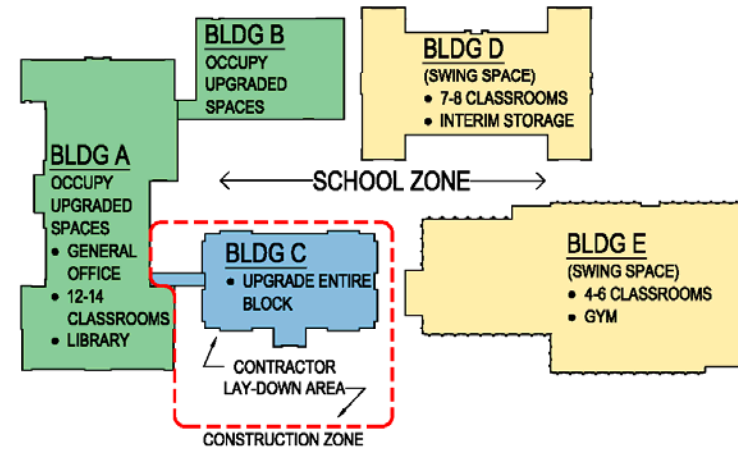

PHASE 3:

- RE-OCCUPY BUILDING 'C'
- VACATE BUILDINGS 'D & E' EXCEPT FOR GYM USE.

